




Scale: 1" = 500'

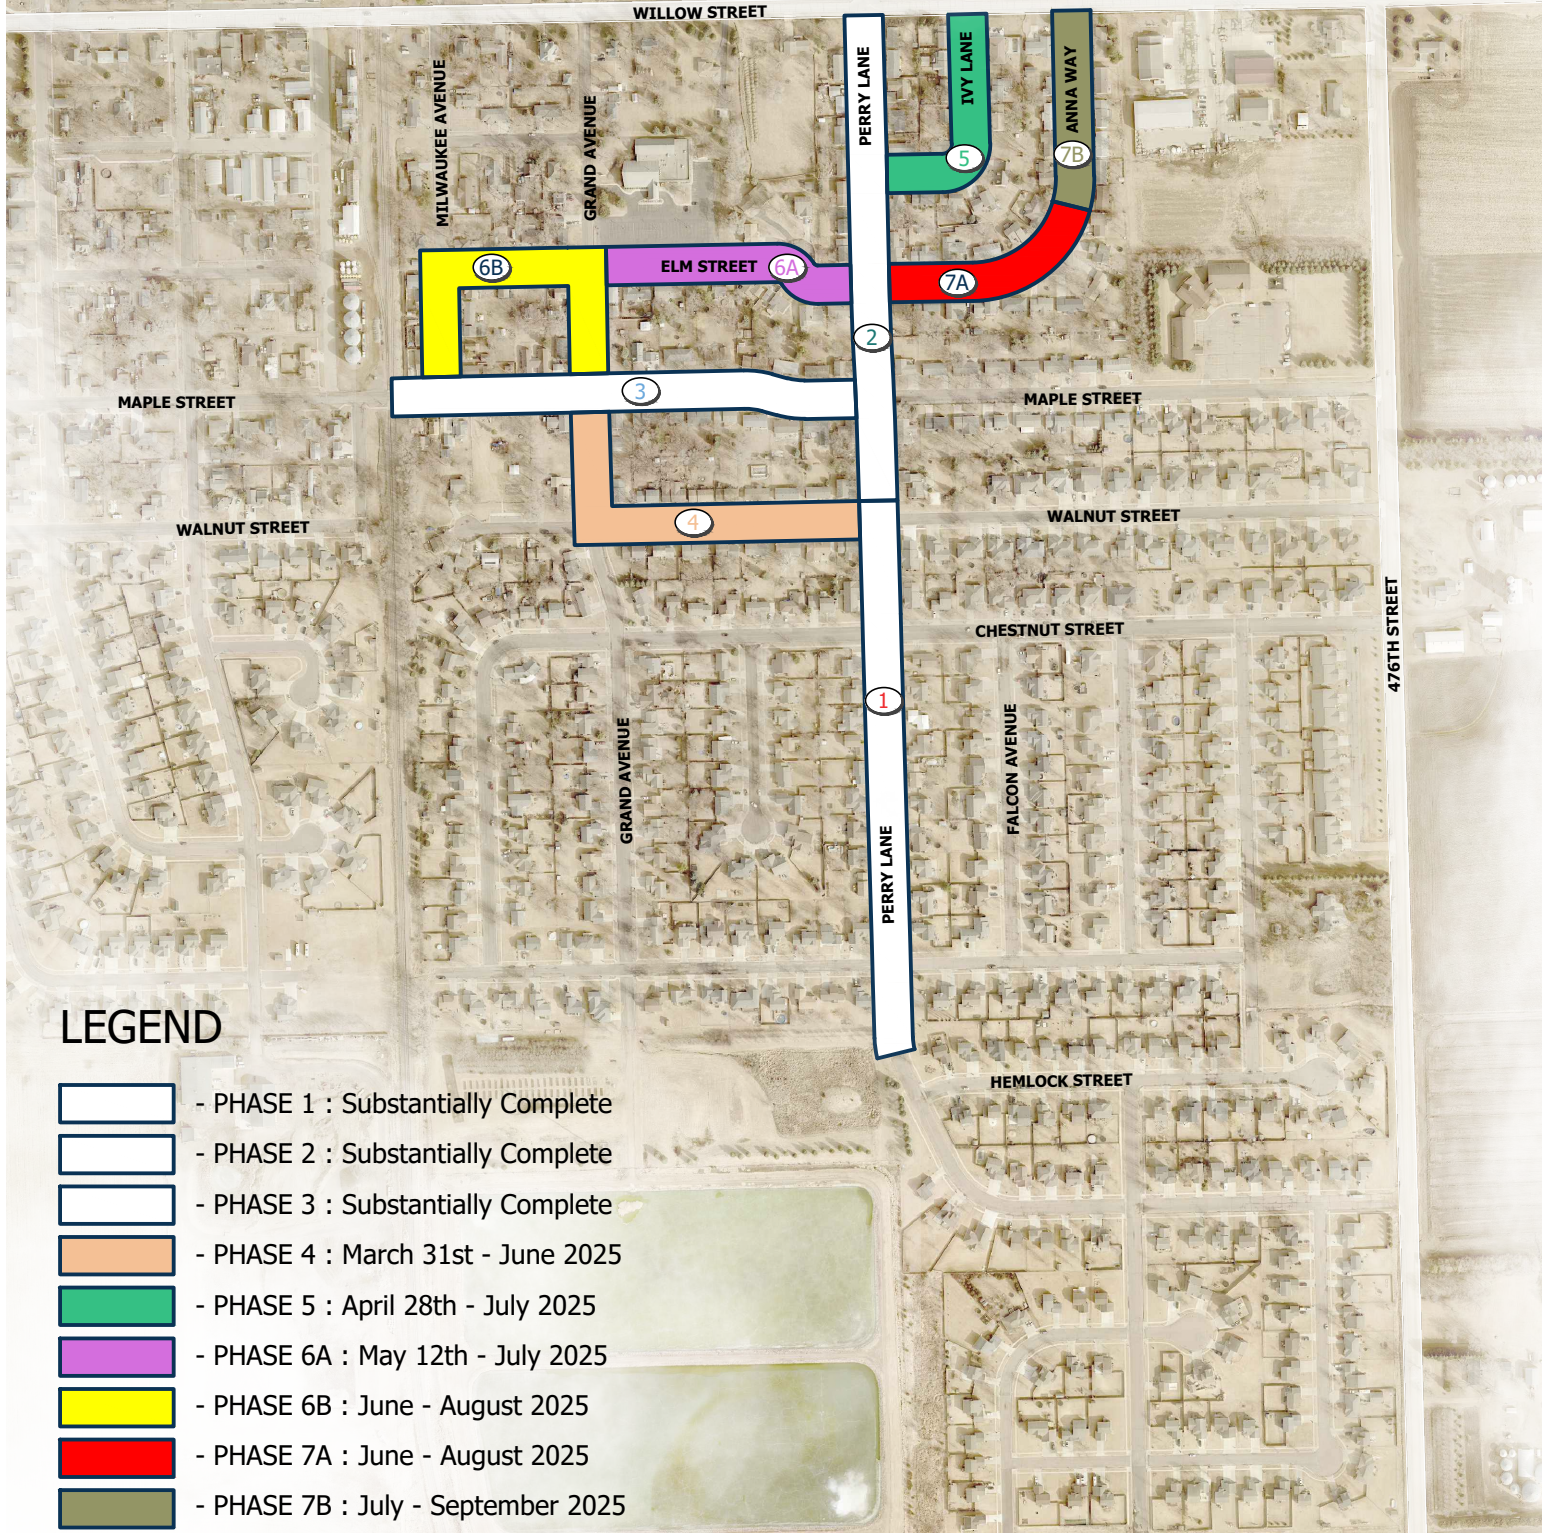

LEGEND

- PHASE 1 : Substantially Complete
- PHASE 2 : Substantially Complete
- PHASE 3 : Substantially Complete
- PHASE 4 : March 31st - June 2025
- PHASE 5 : April 28th - July 2025
- PHASE 6A : May 12th - July 2025
- PHASE 6B : June - August 2025
- PHASE 7A : June - August 2025
- PHASE 7B : July - September 2025

File Location: S:\Projects\2021\21259 - Harrisburg SE Infrastructure Improvements\Inspection Documents\Construction Schedules\Working Files\21259 - Phasing Plan.dwg | Plot Date: 5/19/2025 1:49 PM

Harrisburg SE Infrastructure Improvements Phasing Plan



05/08/2025 SEI#21259

